


2019.04
Interchange 103 Barrier Toll Plaza
Open Road Tolling Conversion
Mile 103
December 12, 2019

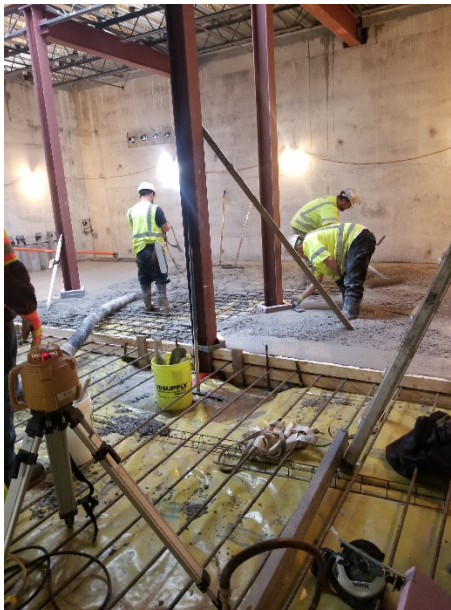

Placing the basement concrete slab in the admin building

Contractor: Sargent Corporation

Bid Amount: \$ 29,888,765.79

Percent Complete last approved pay estimate: 14.7%

Project Schedule: Completion date November 14, 2021.

Project Scope: The work consists of replacing the existing toll plaza; construction of two northbound and two southbound open road tolling (ORT) lanes, and three northbound and three southbound cash/E-ZPass lanes; construction of a precast pedestrian tunnel for employee access and utilities; construction of an Administration Building and access road; reconfiguration of Exit 51 ramps and

I-295 Northbound ramp; and demolition of existing toll plaza and reconstruction of the mainline to accommodate approach and departure grade and alignment differentials at the modified plaza for the Maine Turnpike. The work includes earthwork, pavement, concrete, toll plaza demolition and modification, signing, bridge overpass-mounted, overhead sign structures, concrete barrier, guardrail, electrical work, lighting and lightning suppression systems. The work also includes the installation of tolling provisions in the tunnel, canopy, and toll booth, and maintenance of traffic.

Contractor Schedule: Sargent Corp completed all of the earthwork that they intend to complete for this season. They continue to work on the admin building. Over the next several weeks, the brick façade will be installed, trusses set and interior framing will begin.
