
## 2021.06 New Vehicle Storage Garage - Crosby Maintenance Project Update November 10, 2022

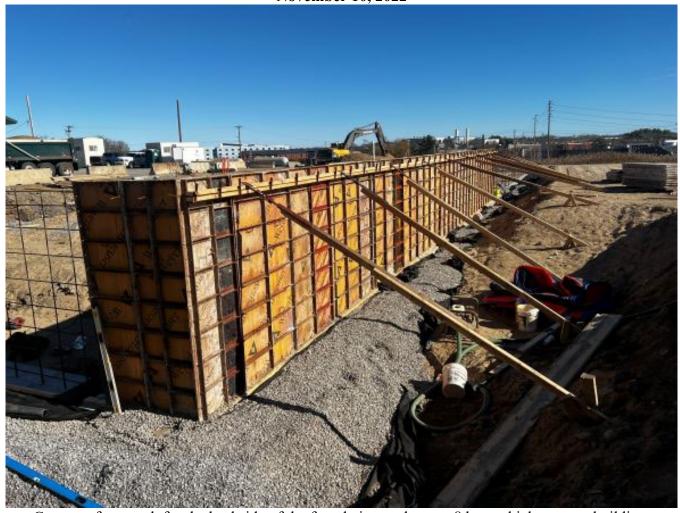

Concrete formwork for the backside of the foundation to the new 8 bay vehicle storage building.

**Contractor:** Doten's Construction **Bid Amount:** \$2,313,000.00

Percent Complete last approved pay estimate: 20.5%

**Project Schedule:** Completion date September 8, 2023.

**Project Scope:** Construction of an approximate 8,800 square foot pre-engineered building consisting of eight (8) vehicle storage garage bays, all site work, paved parking and facility operation areas, generator, power utility services and site utilities.

Contractor Schedule: Site work continues to progress at the new vehicle storage building. Excavation and site preparations for the new building have been ongoing. Currently concrete crews are working on the footing and have starting tying rebar and building forms for the foundation walls. They plan to work on the foundation this fall and will shut down for the winter once the foundation is in place and has been backfilled.
