
2022.13

Bridge Repairs

Route 236 Underpass (MM 1.25)

Route 1 On-Ramp (Ramp H) Underpass (MM 1.60) September, 2023

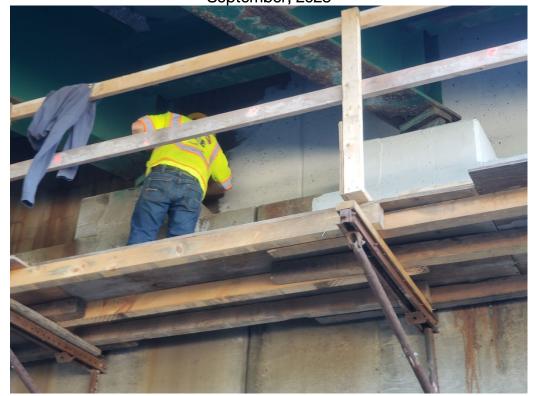

A worker applying pigmented coating to abutment at Route 236.

Contractor: New England Infrastructure, Inc. Bid Amount: \$2,579,980.00

Percent Complete last approved pay estimate: 78.8%

Project Schedule: Completion date November 17, 2023

Project Scope: The work consists of bridge repairs at two locations. At the Route 236 Underpass in the Town of Kittery the work generally includes bridge pavement and membrane replacement, approach work and paving, deck expansion joint modifications, median repairs, bearing cleaning and resetting, bridge drain replacement, slope protection repairs, and miscellaneous superstructure and substructure repairs. At the Route 1 On-Ramp (Ramp H) Underpass in the Town of Kittery the work generally includes bridge pavement and membrane replacement, approach work and paving, deck expansion joint modifications, and miscellaneous superstructure and substructure repairs.

Contractor Schedule: Contractor is finishing up work on the substructure at Route 236. Minor topside work is ongoing.
