
2023.03 Superstructure Replacement at Route 122 August 30, 2024

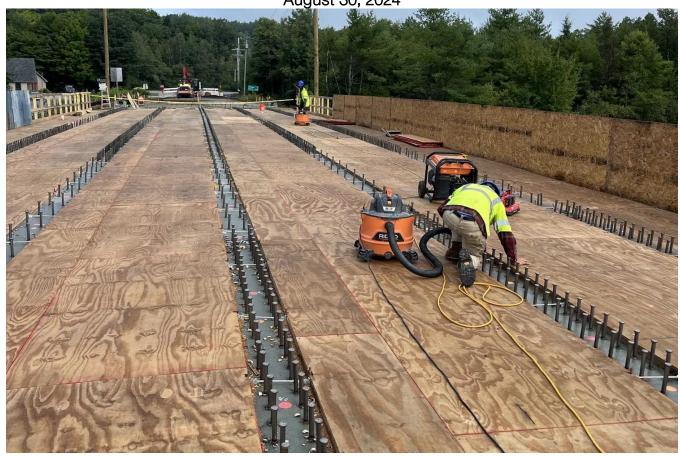

Looking west as crews clean the forms prior to placing reinforcing steel for the deck.

Contractor: CPM Constructors Bid Amount: \$4,679,787.15

Percent Complete last approved pay estimate: 67.3%

Project Schedule: Completion date June 13, 2025

Project Scope: The work consists of bridge repairs to the Eagles Nest Road Southbound Overpass bridge in the Town of Gray, Maine and replacing the Route 122 Underpass bridge over the Maine Turnpike in the City of Auburn, Maine. The work also includes concrete deck and steel girder replacement, concrete substructure modifications and repairs, approach work and paving, and guardrail and bridge rails, at the Route 122 Underpass bridge as well as maintenance of traffic.

Contractor Schedule: The contractor has made continuous progress forming the bridge deck. They have installed all the shear studs (shown above), are tying reinforcing steel, and installing the bridge drains. The crews hope to place the deck in mid-September. The earth work crew has been building the approaches and preparing them for paving at a later date. The contractor is still on schedule to open the bridge in late fall.
