
2024.01
Pavement Rehabilitation Exit 1 to 3 & MM 1.3 to 6.8
June 21, 2024

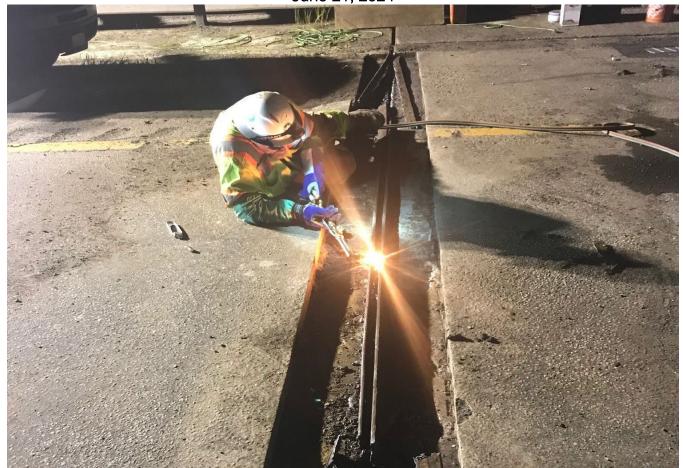

CPM Constructors is removing part of the damaged bridge joint at Spruce Creek Bridge prior to being repaved.

Contractor: Pike Industries, Inc. Bid Amount: \$18,302,432.00

Percent Complete last approved pay estimate: 22.4%

Project Schedule: Completion date July 18, 2025

Project Scope: The work consists of milling and paving the Exits 1, 2, and 3 interchange ramps and mainline from MM 1.3 to MM 6.8, drainage repairs, guardrail, median grading, repairs to the Spruce Creek bridge at MM 2.2, broadcast sealant of York River bridge at MM 5.2, and maintenance of traffic.

Contractor Schedule: Crews have milled all southbound lanes and are milling the northbound lanes. The other crew is working on paving the southbound lanes and should be ready to do the northbound lanes in July. The Spruce Creek bridge bearings and drains have been installed and crews are currently repairing the bridge joints both northbound and southbound.
