


2025.06  
Bridge Repair – Androscoggin River Overpass  
Mile 78.9  
May 23, 2025

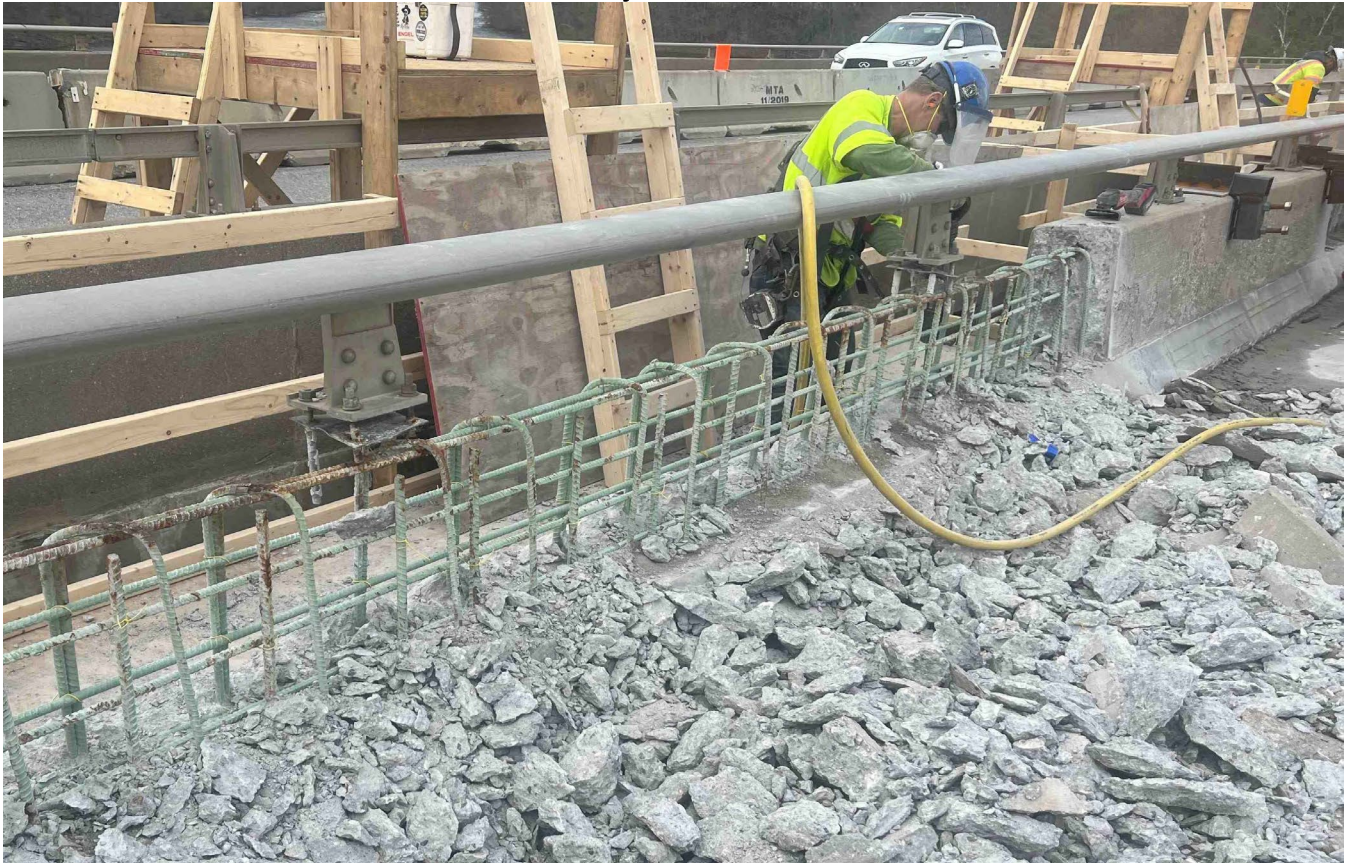

Crews work diligently to remove failing concrete in the northbound parapet

Contractor: CPM Constructors, Inc.

Bid Amount: \$3,680,501

Percent Complete last approved pay estimate: 17.8 %

Project Schedule: Completion date June 18, 2027.

**Project Scope:** The work consists of repairing the Androscoggin River bridge in the Towns of Auburn and Lewiston, Maine. The work includes bridge joint replacement, parapet and railing repairs, parapet and end post rehabilitation, post-tensioning sleeve repair and replacement, bridge deck milling and paving, median approach construction, guardrail replacement, temporary concrete barrier, and maintenance of traffic.

**Contractor Schedule:** Several crews are working on removing deteriorated concrete from the northbound median parapets, they are replacing corroded reinforcing steel, and building forms for the next concrete placement. The earthwork crew is working on median drainage as part of the crossover construction. The crossovers are necessary so that the north end bridge joints can be replaced one at a time. The delivery date of the new bridge joints is unknown at this time.
