


2025.11
Auburn Vehicle Storage Garage
Mile 76.9
August 28, 2026

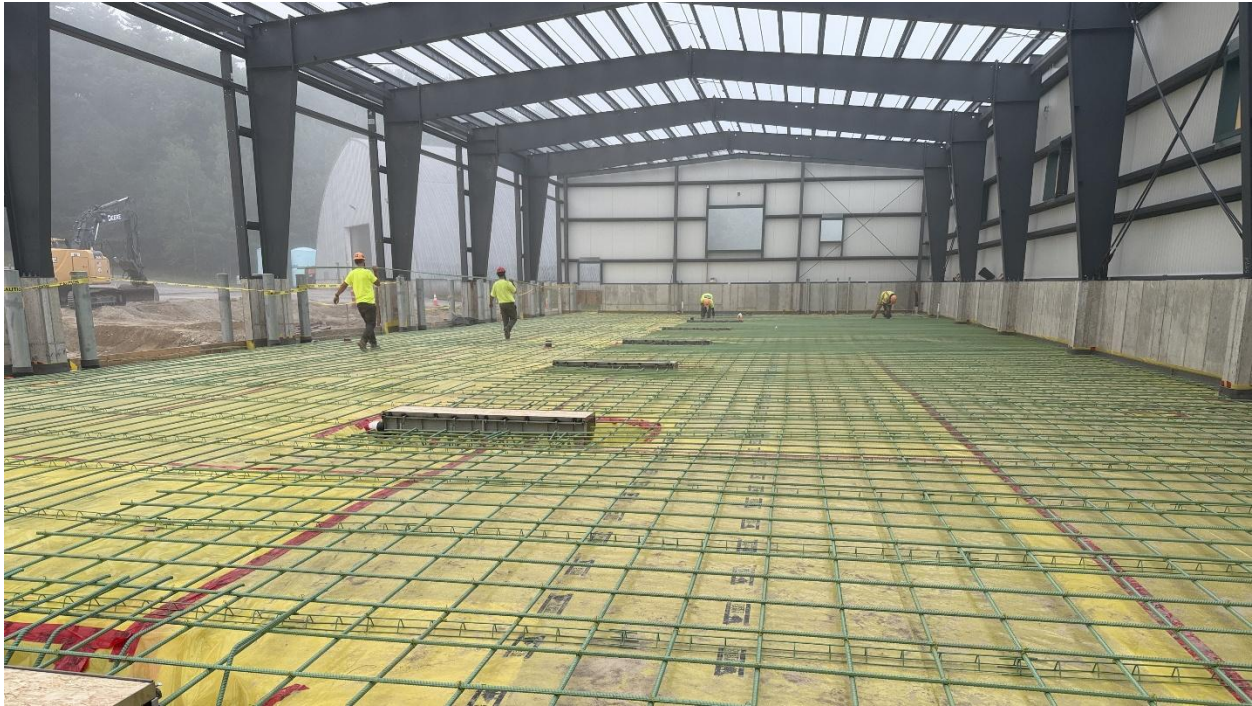

The contractor installs reinforcing steel for the concrete floor slab.

Contractor: Benchmark Construction

Bid Amount: \$3,088,432.00

Percent Complete last approved pay estimate: 47 %

Project Schedule: Completion date November 20, 2026

Project Scope: Construction of an approximate 8,800 square foot pre-engineered building consisting of eight (8) vehicle storage garage bays. All site work including paving, lighting, generator decommissioning and removal, generator installation, relocating propane tanks, floor slab and foundation removal, power utility services and site utilities. The work also includes all building structure, mechanical, electrical, and plumbing, as well as all other work incidental thereto in accordance with the Plans and Specifications.

Contractor Schedule: The contractor continues work on erecting the pre-engineered metal building, frame is complete and exterior siding panels installed on 3 sides. Water holding and oil and water separator tanks were installed. The new electrical service has been established, generator load testing completed, and concrete floor slab placed. Exterior siding panels and roof installation will be the contractor's focus for the month of September. The contractor is trying to mitigate schedule impacts as the project is trending 2 to 3 months behind schedule.
