


2020.06
Emergency Vehicle Ramps - Various Locations
MM 6.2, 10.6 & 19.9 Project Update
August 28, 2020

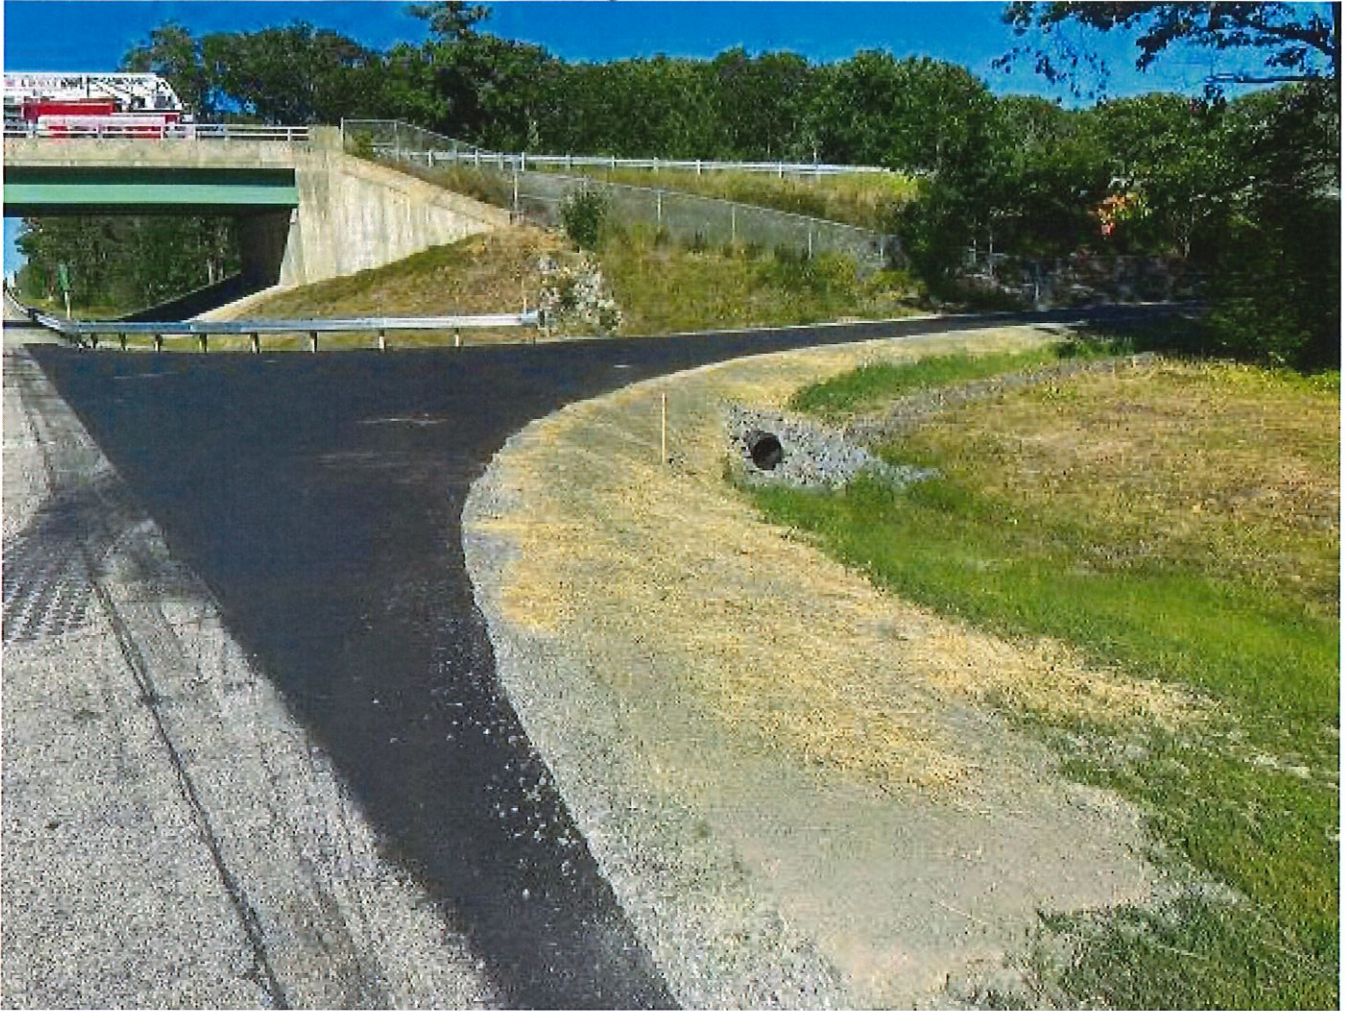

The north bound Burnt Mills Road EVR, with surface pavement and shoulder grading complete.

Contractor: R.J. Grondin & Sons

Bid Amount: \$696,172.00

Percent Complete last approved pay estimate: 84.2%

Project Schedule: Completion date November 20, 2020.

Project Scope: The work consists of constructing two Emergency Vehicle Ramps from Cider Hill Road to the Maine Turnpike in the Town of York, Maine, and constructing two Emergency Vehicle Ramps from Mountain Road to the Maine Turnpike in the Town of York, Maine, and constructing two Emergency Vehicle Ramps from Burnt Mill Road to the Maine Turnpike in the Town of Wells, Maine. The work includes excavation, roadway gravels and pavement, guardrail, and maintenance of traffic.

Contractor Schedule: The contractor has completed the construction of all the EVRs at Burnt Mills, Mountain, and Cider Hill Roads. This includes surface paving, shoulder and slope grading, security gates, and seeding. They are waiting for a new more signs to come in so that they can get installed by their crews. Once the remaining signs are in, the contract will be complete.
