


**2021.07
Project Update
Exit 45 Interchange Reconfiguration
August 27, 2021**

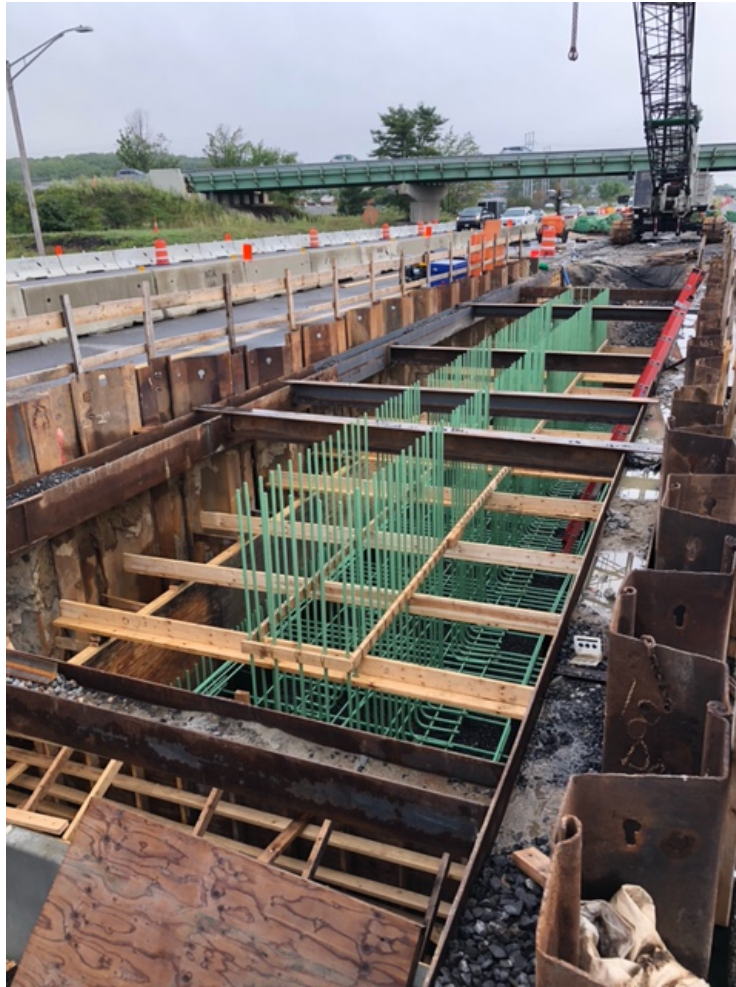

Median pier footing rebar

Contractor: CPM Constructors

Bid Amount: \$ 27,673,714.90

Percent Complete last approved pay estimate: 16.2%

Project Schedule: Completion date September 1, 2023

Project Scope: The work consists of highway, bridge and toll system construction at Exit 45 South Portland Interchange. The work includes a new bridge, new southbound and northbound ramps, a new southbound toll plaza on the west side of the Maine Turnpike with a signalized intersection and a new northbound toll plaza on the east of the Maine Turnpike, Route 703 reconstruction, demolition of the existing toll plaza and bridge.

Contractor Schedule: CPM Constructors is working on the northbound on-ramp toll building wall and installing the new toll booths. The southbound on-ramp toll plaza work continues with placing approach slabs and building foundation walls. The median pier for the new bridge concrete footing has been placed and various earthwork activities are ongoing.
