


2025.17
Bridge Repair – Saco River Overpass: Mile 78.9
Forest Avenue Emergency Repairs: Mile 50.0
November 14, 2025

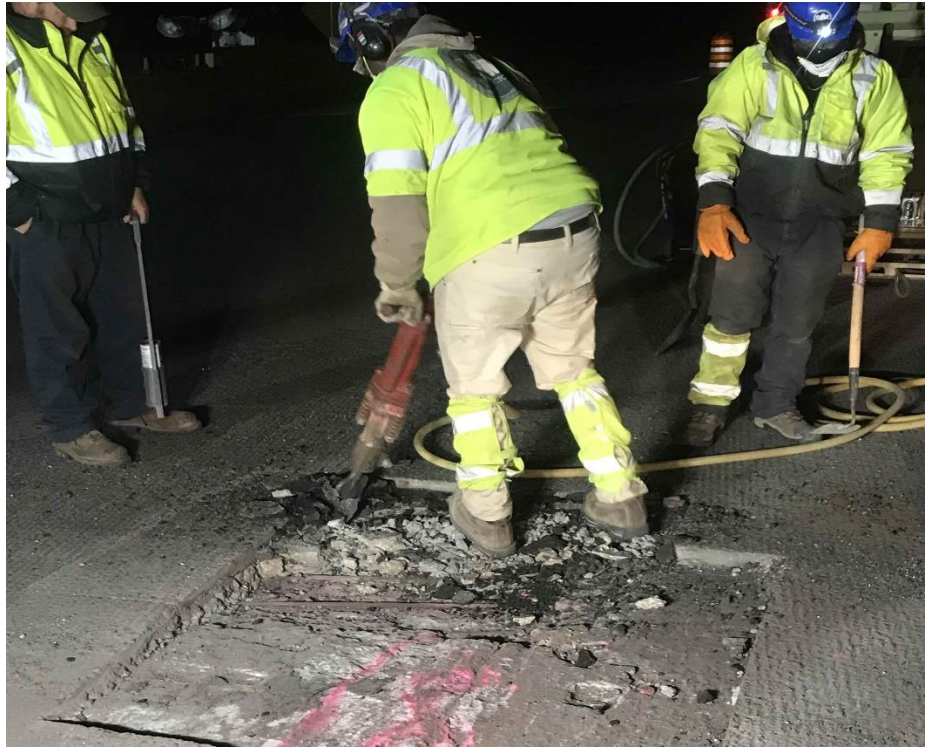

A laborer uses a jack hammer to remove loose concrete from the southbound Forest Avenue bridge.

Contractor: CPM Constructors, Inc.

Bid Amount: \$1,638,885.84

Percent Complete last approved pay estimate: 13.2 %

Project Schedule: Completion date June 26, 2026.

Project Scope: The work consists of removing and reconstructing the concrete curbs on both sides of the southbound Saco River bridge, installing new railing anchorage and resetting the existing 2-bar aluminum bridge rail. The work at Forest Avenue bridge consists of removing pavement surface, partial depth and full depth deck chipping and patching, deck membrane repair, paving, asphaltic plug joint removal and reinstallation, and maintenance of all required traffic control devices.

Contractor Schedule: The contractor has performed all the top side concrete repairs and has paved the Forest Avenue bridge. Currently they are working on the overhead concrete repairs from Forest Avenue. A second crew is mobilizing to the SB Saco River bridge to start setting up traffic control for the future curb and bridge rail repairs over the winter.
