
2026.06
Bridge Repairs – Wells and Kennebunk
Mile 19.9, 21.7, 23.6 and 24.7
October 8, 2026

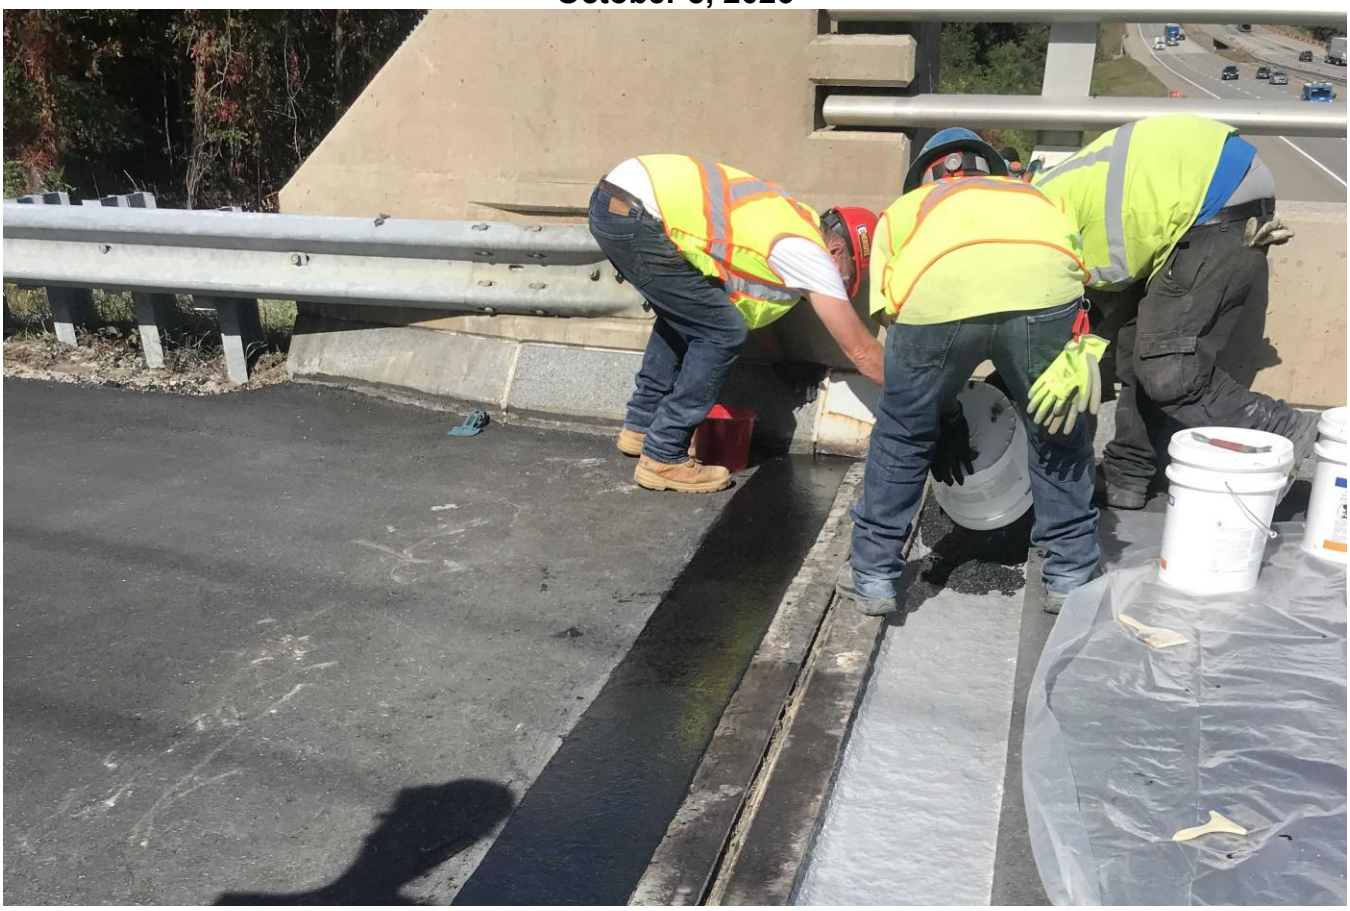

The contractor is installing elastomeric concrete joint header material at Cat Mousam Road Bridge in Kennebunk.

Contractor: CPM Constructors, Inc. **Bid Amount:** $1,891,406.10

Percent Complete last approved pay estimate: 34 %

Project Schedule: Completion date November 20, 2026.

Project Scope: The work consists of general repairs and modifications to Burnt Mill Road Underpass Bridge at Mile 19.9, Coles Hill Road Underpass at Mile 21.7, High Street Underpass at Mile 23.6, and Cat Mousam Road Underpass at Mile 24.7. The work includes milling and filling the bituminous wearing surfaces at all locations, parapet joint repairs and bridge joint repairs at Coles Hill Road, High Street, and Cat Mousam Road, haunch concrete removal at Burnt Mill Road, approach work and paving, maintenance of traffic and all other work incidental thereto in accordance with the plans and specifications.

Contractor Schedule: The contractor has completed the topside bridge deck rehabilitation on the four bridges and the contractor will continue underside bridge repairs with mainline lane closures into November 2026.
