
2025.11
Auburn Vehicle Storage Garage
Mile 76.9
November 13, 2026

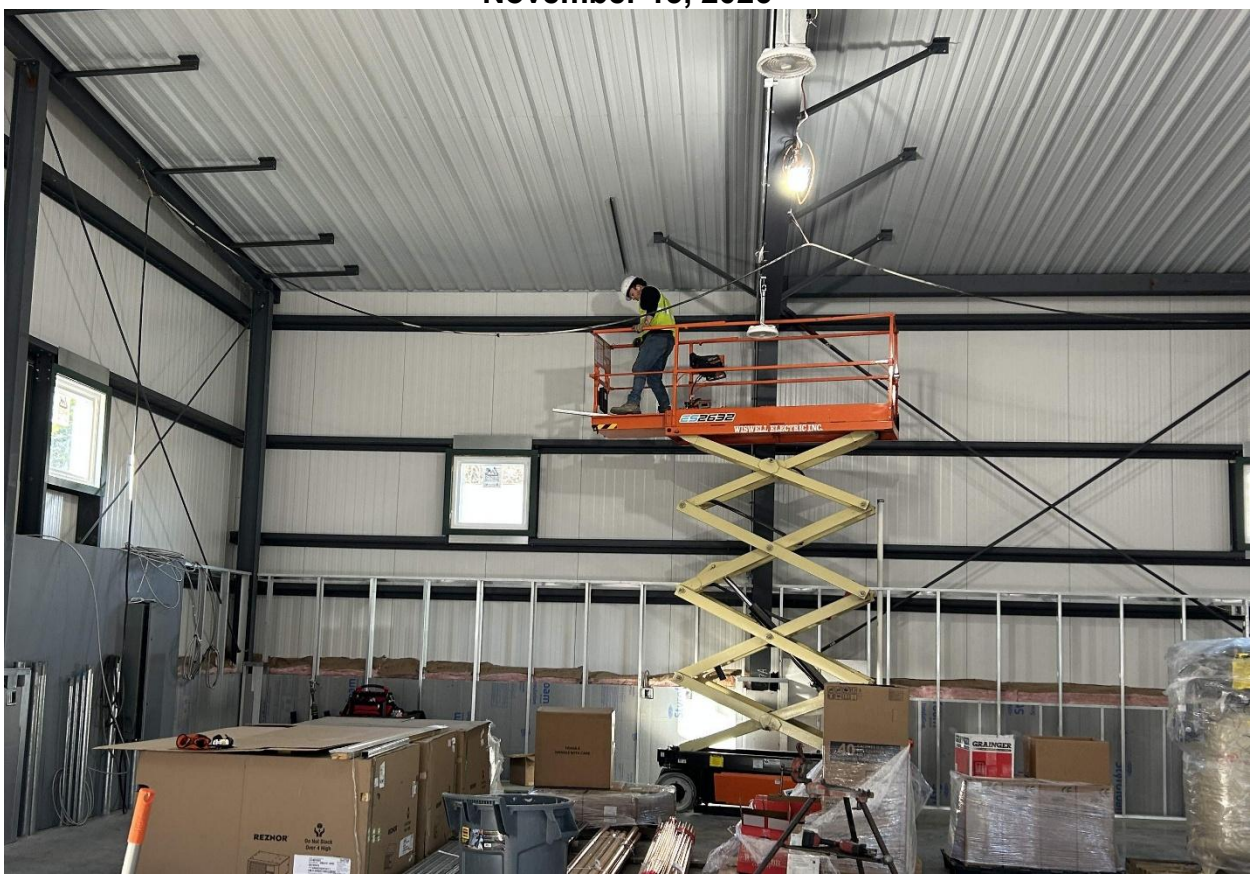

The contractor installs some conduits for future interior lighting.

Contractor: Benchmark Construction **Bid Amount:** $3,088,432.00

Percent Complete last approved pay estimate: 77.2 % **Date:** 11-5-2026

Project Schedule: Completion date November 20, 2026

Project Scope: Construction of an approximate 8,800 square foot pre-engineered building consisting of eight (8) vehicle storage garage bays. All site work including paving, lighting, generator decommissioning and removal, generator installation, relocating propane tanks, floor slab and foundation removal, power utility services and site utilities. The work also includes all building structure, mechanical, electrical, and plumbing, as well as all other work incidental thereto in accordance with the plans and specifications.

Contractor Schedule: Inside the 8-bay, mechanical and electrical sub-contractors are working on conduit, lighting, and HVAC systems. Other crews are finishing the interior liner panels and interior the half wall. On the exterior, crews have finished the snow guards and other metal trim work. The contractor has also placed the surface course pavement and is working on the final grading around the new building. The project is trending 2 to 3 months behind schedule.
