
2025.17
Bridge Repair – Saco River Overpass: Mile 78.9
Forest Avenue Emergency Repairs: Mile 50.0
November 13, 2026

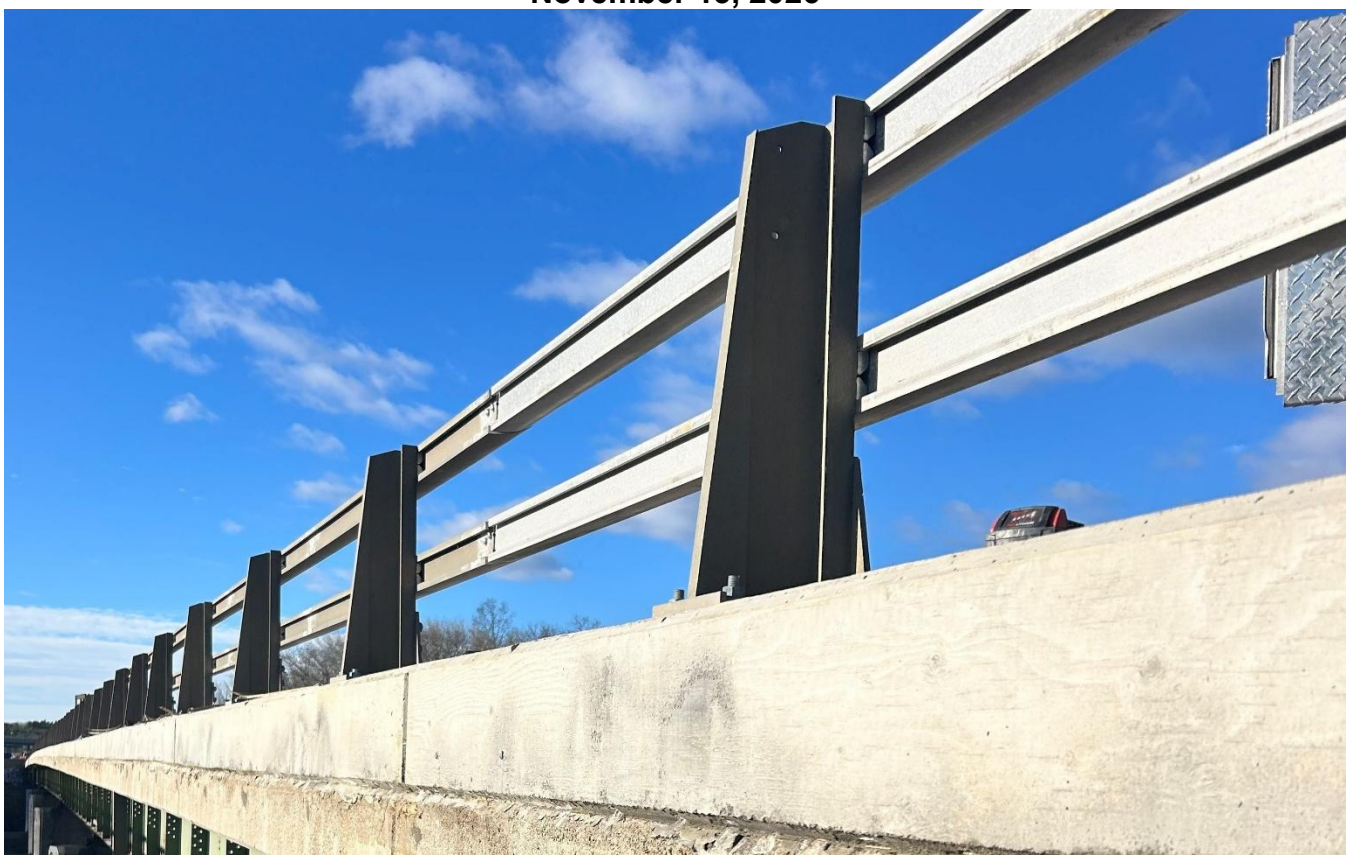

Looking south at the backside of the new concrete curb and reinstalled bridge rail.

Contractor: CPM Constructors, Inc. **Bid Amount:** $1,638,885.84

Percent Complete last approved pay estimate: 83.2% **Date:** 10-22-2026

Project Schedule: Completion date December 2, 2026.

Project Scope: The work consists of removing and reconstructing the concrete curbs on both sides of the southbound Saco River bridge, installing new railing anchorage and resetting the existing 2-bar aluminum bridge rail. The work at Forest Avenue bridge consists of removing pavement surface, partial depth and full depth deck chipping and patching, deck membrane repair, paving, asphaltic plug joint removal and reinstallation, and maintenance of all required traffic control devices.

Contractor Schedule: The contractor has replaced all the concrete curb as shown on the plans. The bridge rail has been reinstalled for the entire length of the bridge. They have removed the concrete barrier, temporary forms, and all safety rails now that it is safe to do so. This project should be complete by the end of November.
